


Maritime Industrial Expansion / Norton Terminal Development & MTCA 3rd Interim Action – Construction Progress Update

John Klekotka Port of Everett January 5, 2022





PROJECT SITE DEVELOPMENT

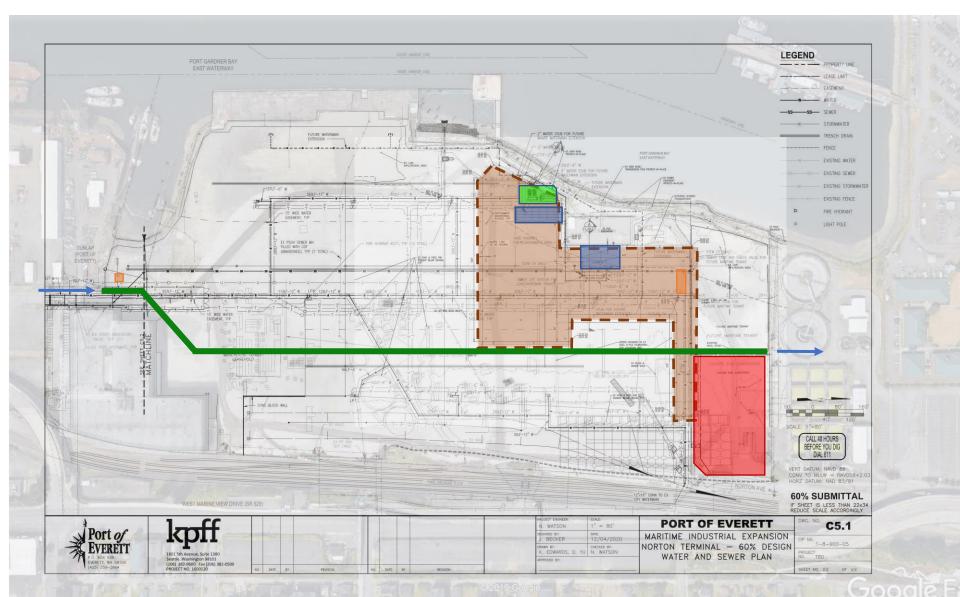

GENERAL PROGRESS

- SRV completed preload in early Nov. Have yet to see any significant settlement. Contract closeout next month
- Strider mobilized in late Oct and started work in early Nov. Primarily working on demolition of misc items and known underground pipes; beginning work on waterlines
- City has bid their pipeline project and Council awarded to NW Construction Co.; pipe materials being ordered and onsite work to begin in March
- Various construction issues such as wet conditions, weather, unexpected underground conditions, and pockets of contamination
- On track for completion in Oct.
- Next week will request approval for another contract modification with KPFF Engineers for ongoing work mostly related to the existing warehouse redevelopment









QUESTIONS OR COMMENTS?

THANK YOU!

REAL STR.
