


Bay Wood Interim Action - Shoreline Restoration and Cleanup Project

Erik Gerking | Director of Environmental Programs January 12, 2021






BAY WOOD INTERIM ACTION

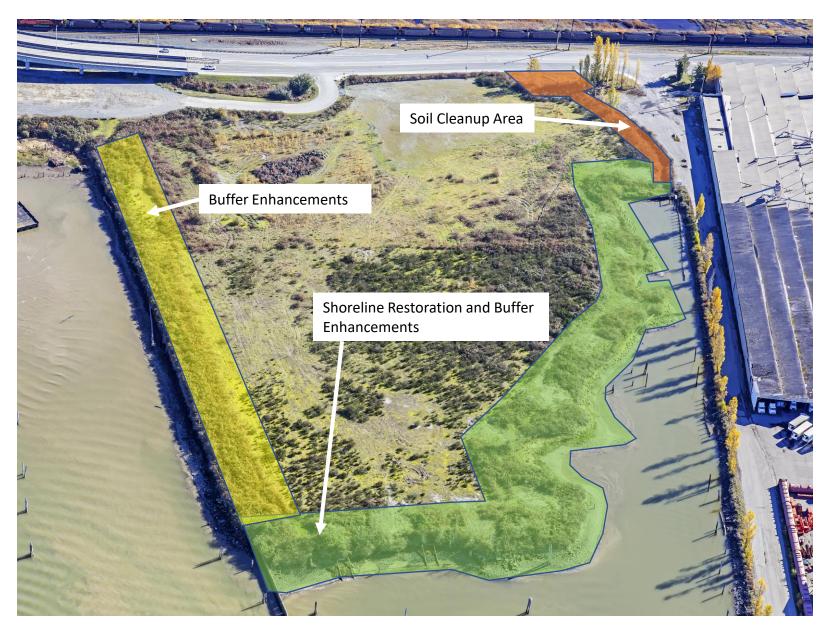

BAY WOOD (December 29, 2020)

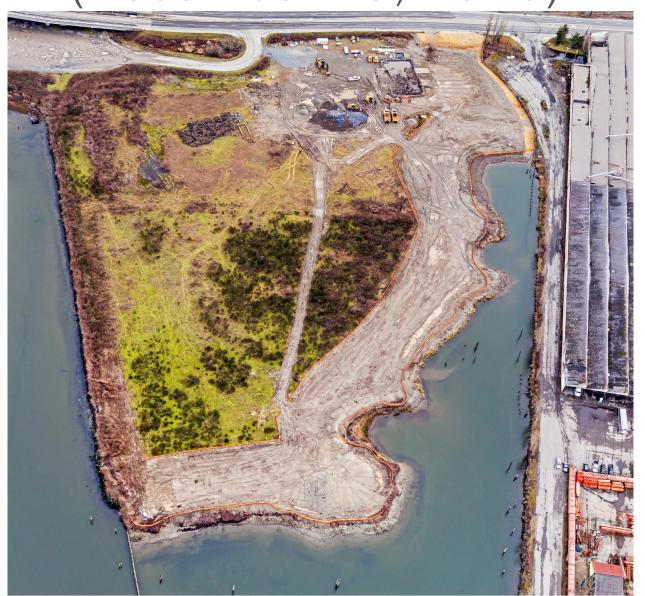





Western Shoreline (Pre-Restoration)



Western Shoreline (Jan 6, 2021)



Southern Shoreline (Pre-Restoration)




Southern Shoreline (January 11, 2021)



Southern Shoreline



RESTORATION AND PUBLIC ACCESS

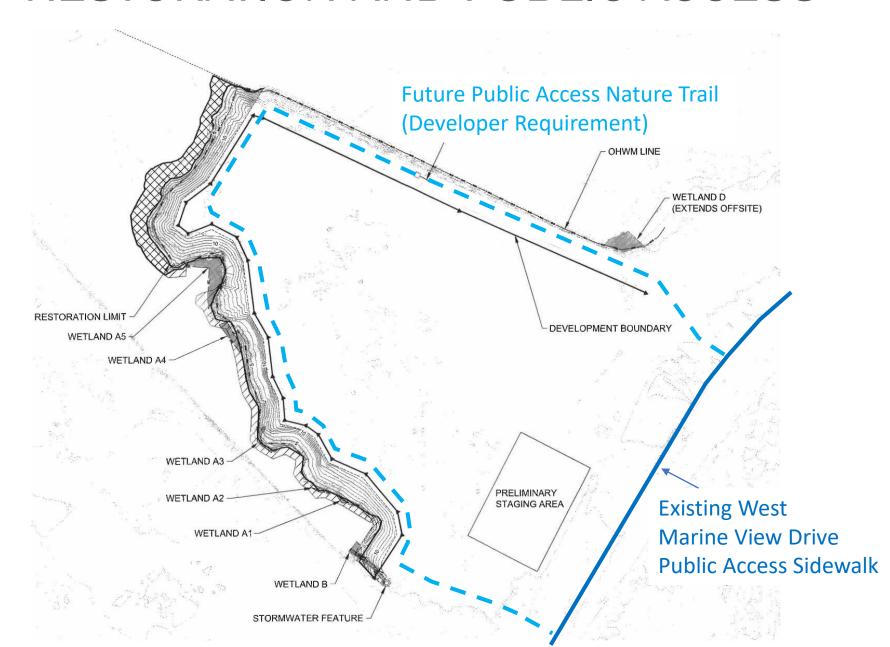

CURRENT SITE LAYOUT



Project Status

- Completed Low Area cleanup
- Completed lower bank shoreline grading
- Change Order Requests:
 - 1. Time Delay Due to Extended Ecology Construction Stormwater Permitting Process
 - 2. Ecology Required Soil Mixing Due to Topsoil Chemistry
- Material Quantities: some over-runs and under-runs. Over-runs are related to additional excavation as requested by Ecology
- Remaining Work: 1) Upper Bank Grading, 2) Placing Logs, and
 3) Planting
- Anticipated to complete on-time (April 1, 2021)

THANK YOU! QUESTIONS?





THANK YOU!



@portofeverett | #portofeverett
