



**SEA THE
FUTURE
WITH US**

Request to Closeout Bay Wood Interim Action - Shoreline Restoration

Elise Gronewald | Project Manager


September 14, 2021



@portofeverett | #portofeverett



BAY WOOD INTERIM ACTION

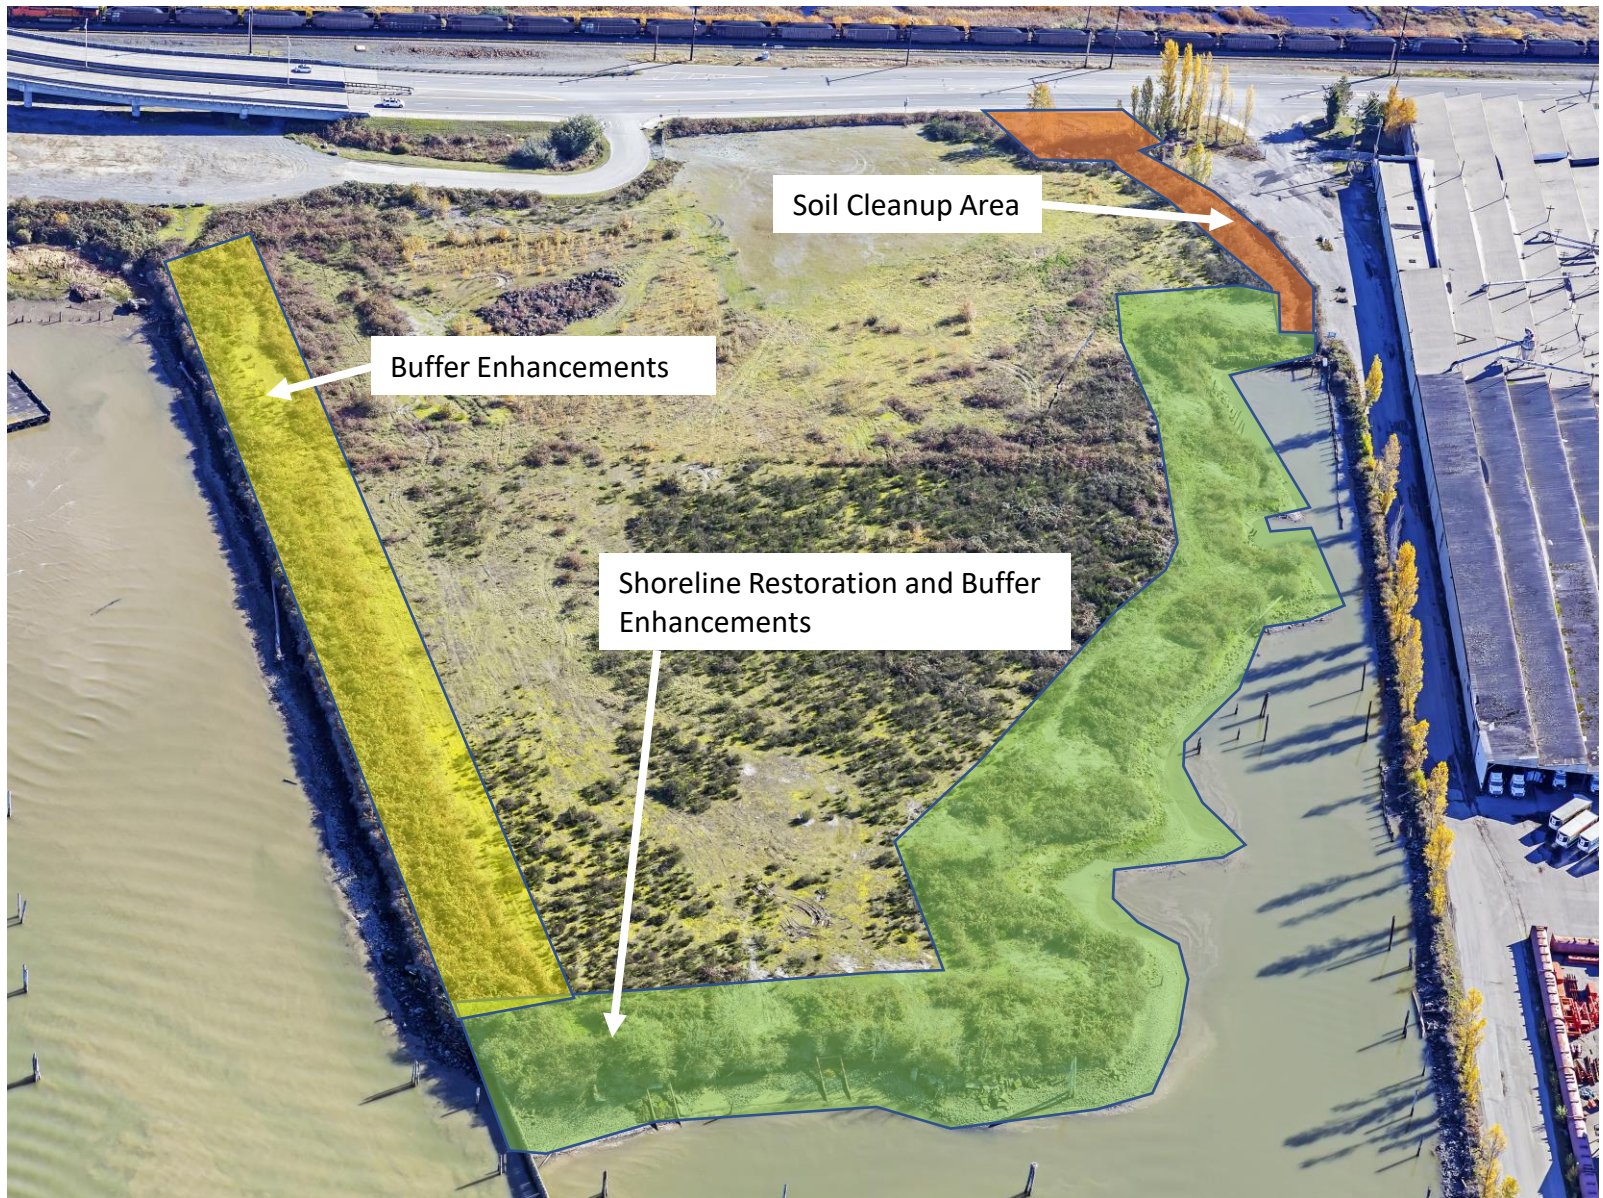

HIGHLIGHTS

- Project awarded by Commission to Strider on September 13, 2020
- Crew was onsite and working beginning in late Nov/early Dec of 2020
- Approx. 4,400 Tons of contaminated material removed from the site
- 1,300 LF of Shoreline re-graded and re-planted and 2,200 LF of upper bank re-graded and re-planted

WEST SHORELINE (POST RESTORATION)



CONSTRUCTION COST SUMMARY

	Original Bid	Final Amount
Original Bid	\$ 1,398,213.00	\$ 1,426,393.61
Change Orders		
01		\$ 44,279.66
02		\$ 36,899.76
Over Runs / (Under Runs)	-	\$ (52,998.81)*
Subtotal		\$ 1,426,393.61
WSST	\$ 137,024.87	\$ 139,786.57
Total	\$ 1,535,237.87	\$ 1,566,180.10

* Final contract reconciliation change order amount

REQUESTED COMMISSION ACTION

Commission authorize closeout of the public works contract for the Bay Wood Interim Action - Shoreline Restoration and Cleanup project with Strider Construction in the amount of \$1,566,180.18, including Washington State sales tax.

THANK YOU! QUESTIONS?





NEXT 100

WE PROVIDE VALUE: WE CREATE ECONOMIC OPPORTUNITIES

THANK YOU!



@portofeverett | #portofeverett
