# MILLWRIGHT LOOP CONSTRUCTION SEQUENCING PHASE 1 | ANTICIPATED TIMELINE: MARCH – JULY 2023

## PHASE 1 SCOPE

- First phase of preload placed and settling
- Marina Fuel Tank preload placed and settling
- Construction Zone Traffic Route Modifications
- Construction of Temporary Access Roads
- Temporary realignment of Marina & Visitor Parking

### **PROJECT KEY**

TEMPORARY ROAD

SHUTTLE LOT

SLIPHOLDER PARKING

VISITOR PARKING

CONSTRUCTION ZONE



MARINA SLIPHOLDER SHUTTLE LOT & DROPOFF LOCATIONS





Port to implement shuttle service for boaters due to increased parking impacts during peak season; more information to follow



Temporary utility impacts to be expected; slipholders to receive AlertSense notifications





#### **QUESTIONS?**

# MILLWRIGHT LOOP CONSTRUCTION SEQUENCING PHASE 2 | TIMELINE: JULY 2023 - FEBRUARY 2024

## PHASE 2 SCOPE

- Regrading preload piles
- Installing all new utilities
- Building Millwright Loop North and South, as well as Chamfer Street

## **PROJECT KEY**

TEMPORARY ROAD

SHUTTLE LOT (THROUGH SEPTEMBER)

SLIPHOLDER PARKING

VISITOR PARKING

CONSTRUCTION ZONE

MARINA SLIPHOLDER SHUTTLE LOT & DROPOFF LOCATIONS





Port to continue shuttle service for boaters due to increased parking impacts; more information to follow



Closure of the Central Marina restroom; repurpose former Milltown Sailing building with restrooms and free laundry for slipholders



Restroom and showers open at new Central Marina restroom near Hotel Indigo



Temporary utility impacts to be expected; slipholders to receive AlertSense notifications





#### **QUESTIONS?**

# MILLWRIGHT LOOP **CONSTRUCTION SEQUENCING** PHASE 3 | TIMELINE: FEBRUARY 2024 – MAY 2024

## PHASE 3 SCOPE

- Construct new Marina Slipholder parking lot adjacent to eastern gatehouse
- Construct eastern esplanade expansion and vista

### **PROJECT KEY**

TEMPORARY ROAD

COMPLETED ROAD

SHUTTLE LOT

SLIPHOLDER PARKING

VISITOR PARKING

BRIEF CLOSURE

CONSTRUCTION ZONE




MARINA SLIPHOLDER SHUTTLE LOT & DROPOFF LOCATIONS

> Port to continue shuttle service for boaters due to increased parking impacts

New Millwright Loop North, South and Chamfer Streets open for use





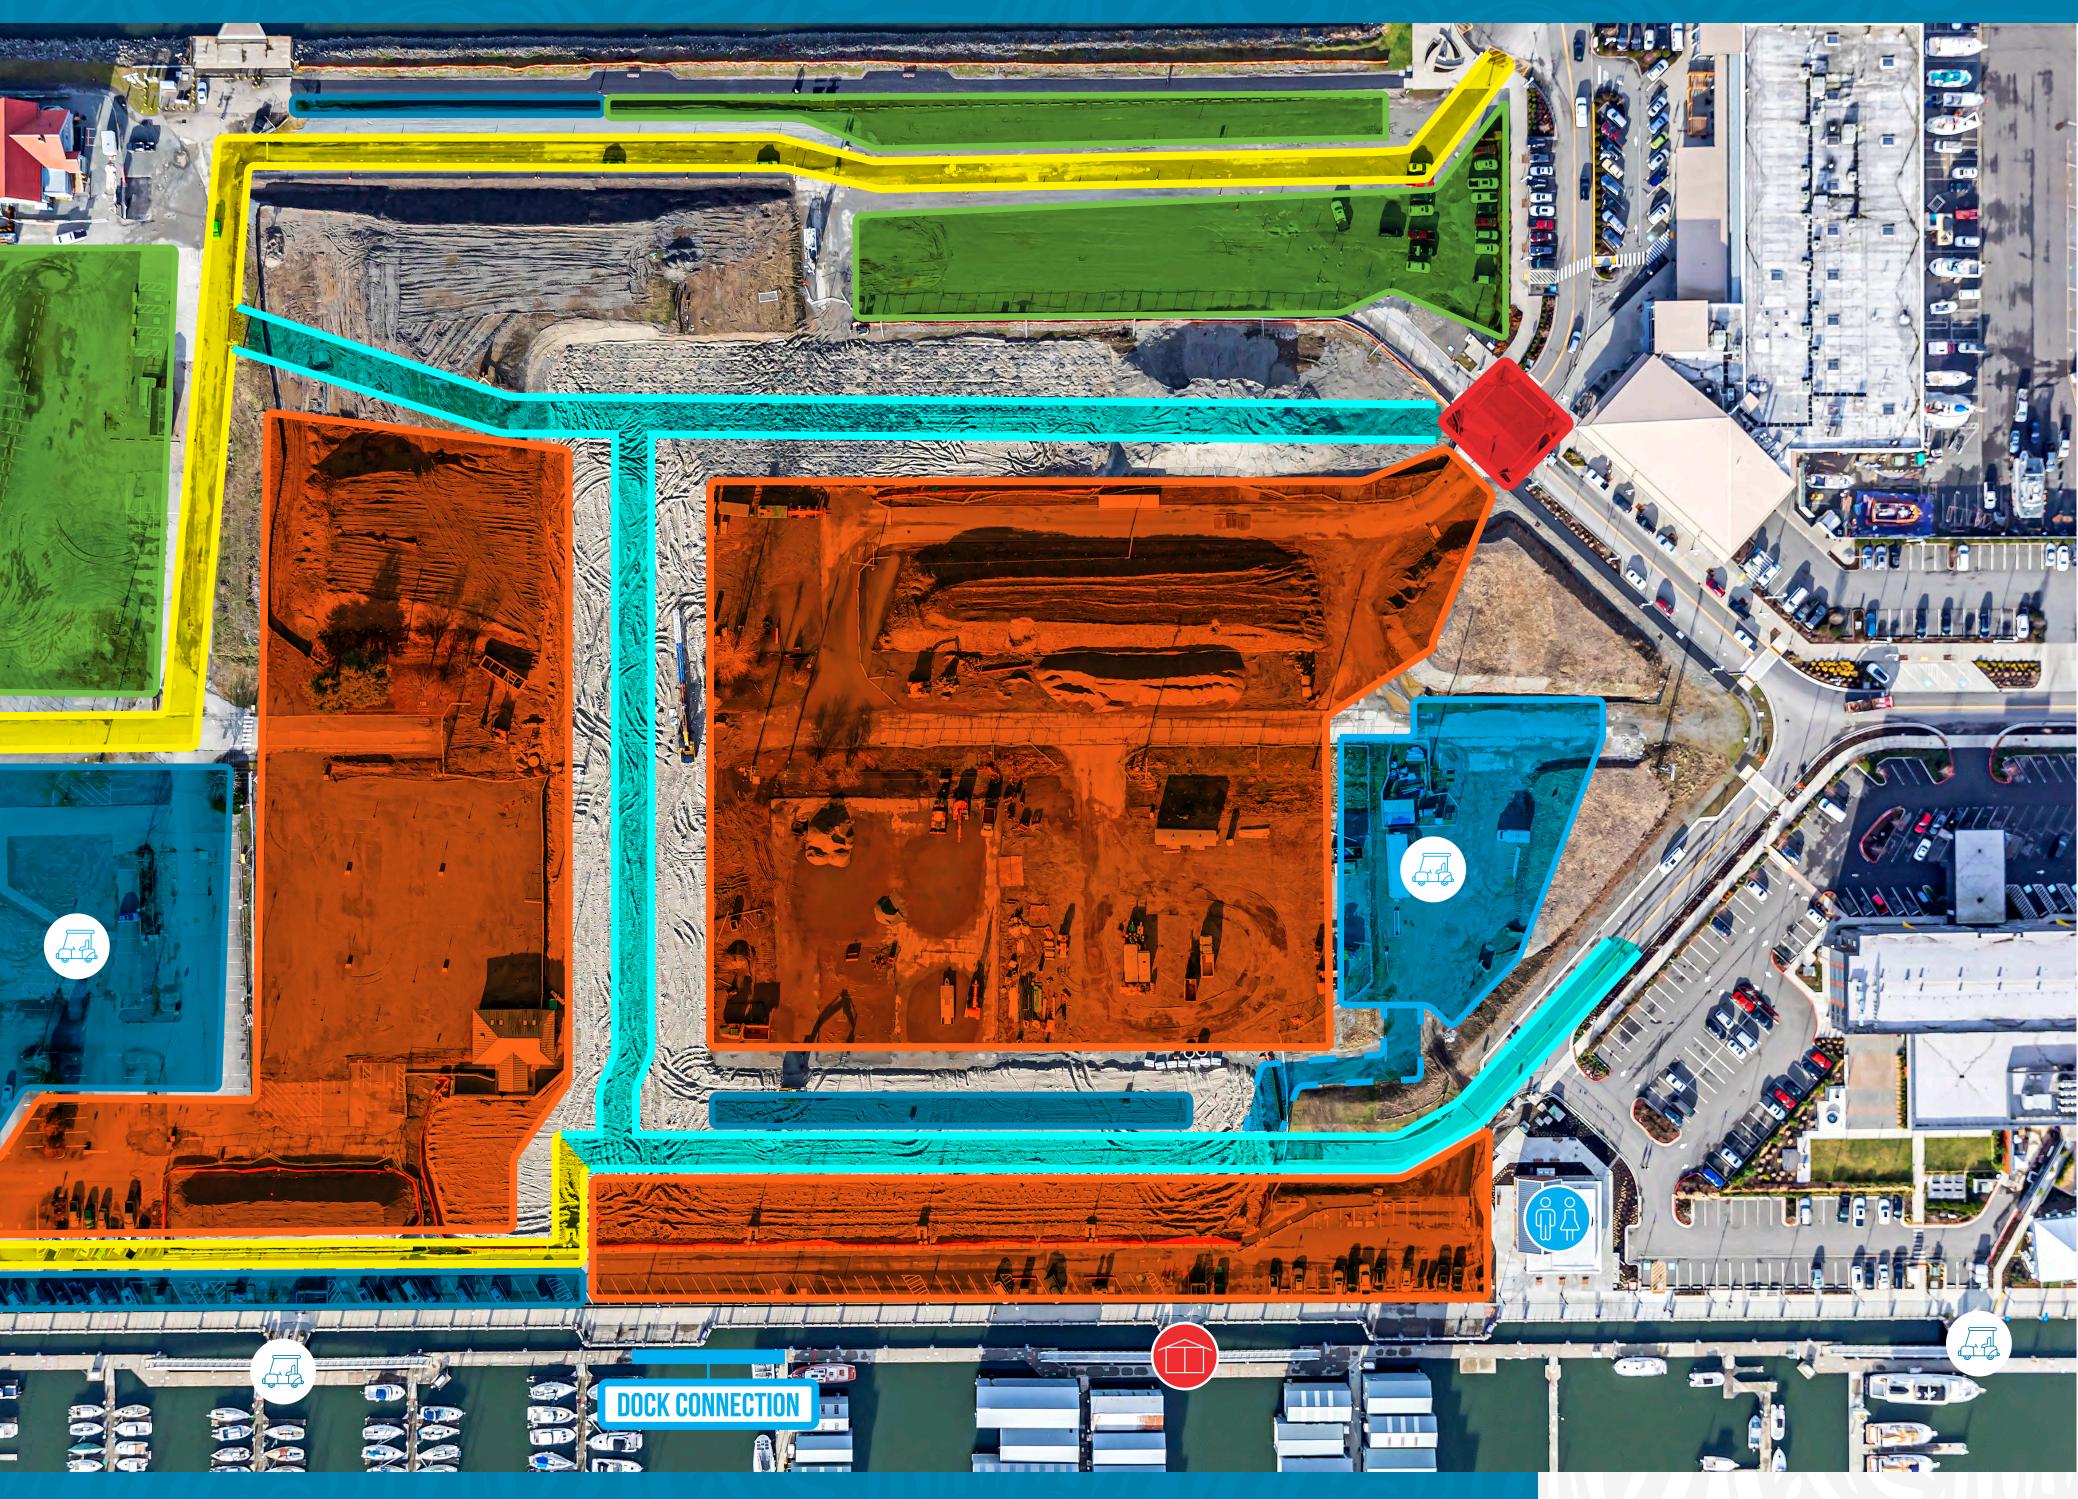



travel restored



Anticipated temporary 10-day closure of access to Central G - J Docks gatehouse; advance notice and alternate access provided







Temporary utility impacts to be expected; slipholders to receive AlertSense notifications

#### **QUESTIONS?**

# MILLWRIGHT LOOP **CONSTRUCTION SEQUENCING** PHASE 4 | TIMELINE: MAY 2024 – JULY 2024

## **PHASE4** SCOPE

- Construct final segment of Millwright Loop (roadways, utilities)
- **Construct new Marina** Slipholder parking lot adjacent to western gatehouse
- Construct western esplanade expansion and vista

### **PROJECT KEY**

TEMPORARY ROAD

COMPLETED ROAD

SHUTTLE LOT (IF NEEDED)


SLIPHOLDER PARKING

VISITOR PARKING

CONSTRUCTION ZONE



MARINA SLIPHOLDER SHUTTLE LOT & DROPOFF LOCATIONS

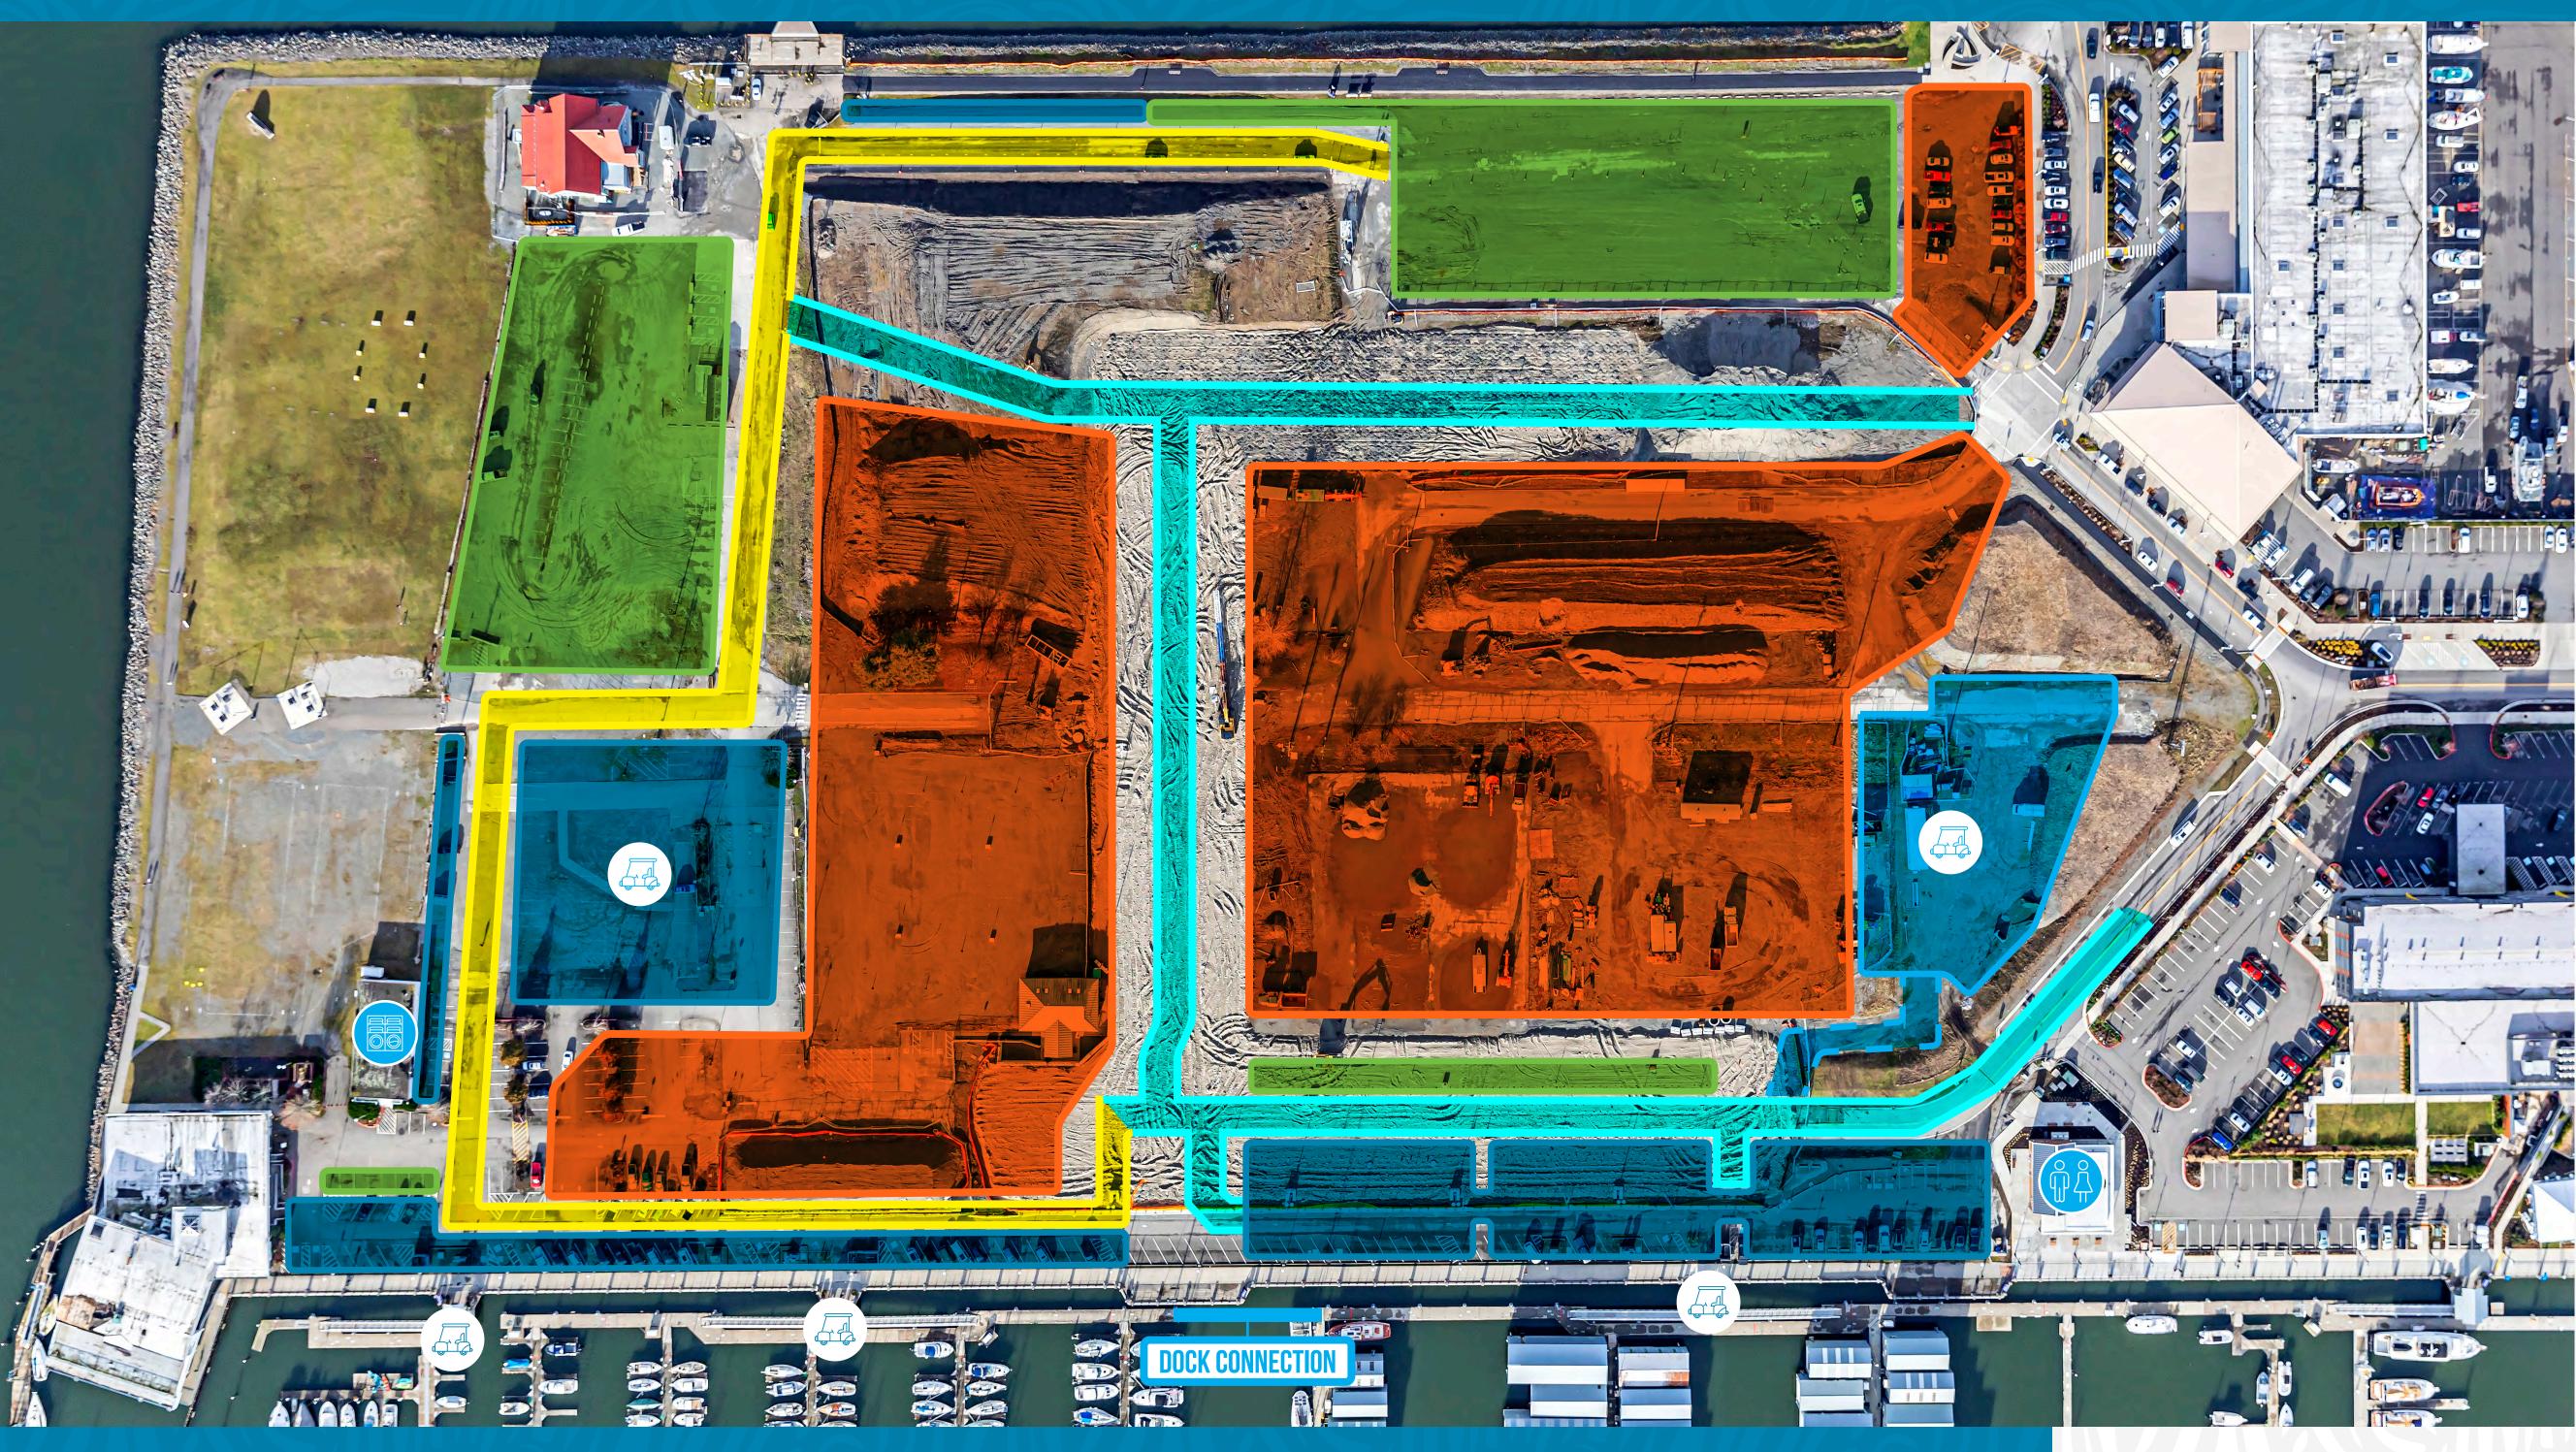



Port to continue shuttle service for boaters due to increased parking impacts; service will continue until it is no longer in demand; more information to follow



New eastern gated Marina Slipholder Parking Lot open



Two-way travel restored



Temporary utility impacts to be expected; slipholders to receive AlertSense notifications





#### **QUESTIONS?**

# MILLWRIGHT LOOP **CONSTRUCTION SEQUENCING** PHASE 5 | TIMELINE: JULY 2024 - NOVEMBER 2024

## **PHASE 5** SCOPE

- Construct final segment of Millwright Loop South (roadways, utilities)
- Build western Marina Slipholder parking lot
- Construct western esplanade expansion and vista

### **PROJECT KEY**

TEMPORARY ROAD

COMPLETED ROAD

SHUTTLE LOT (IF NEEDED)


SLIPHOLDER PARKING

VISITOR PARKING

CONSTRUCTION ZONE



SHUTTLE PARKING & DROPOFF LOCATIONS

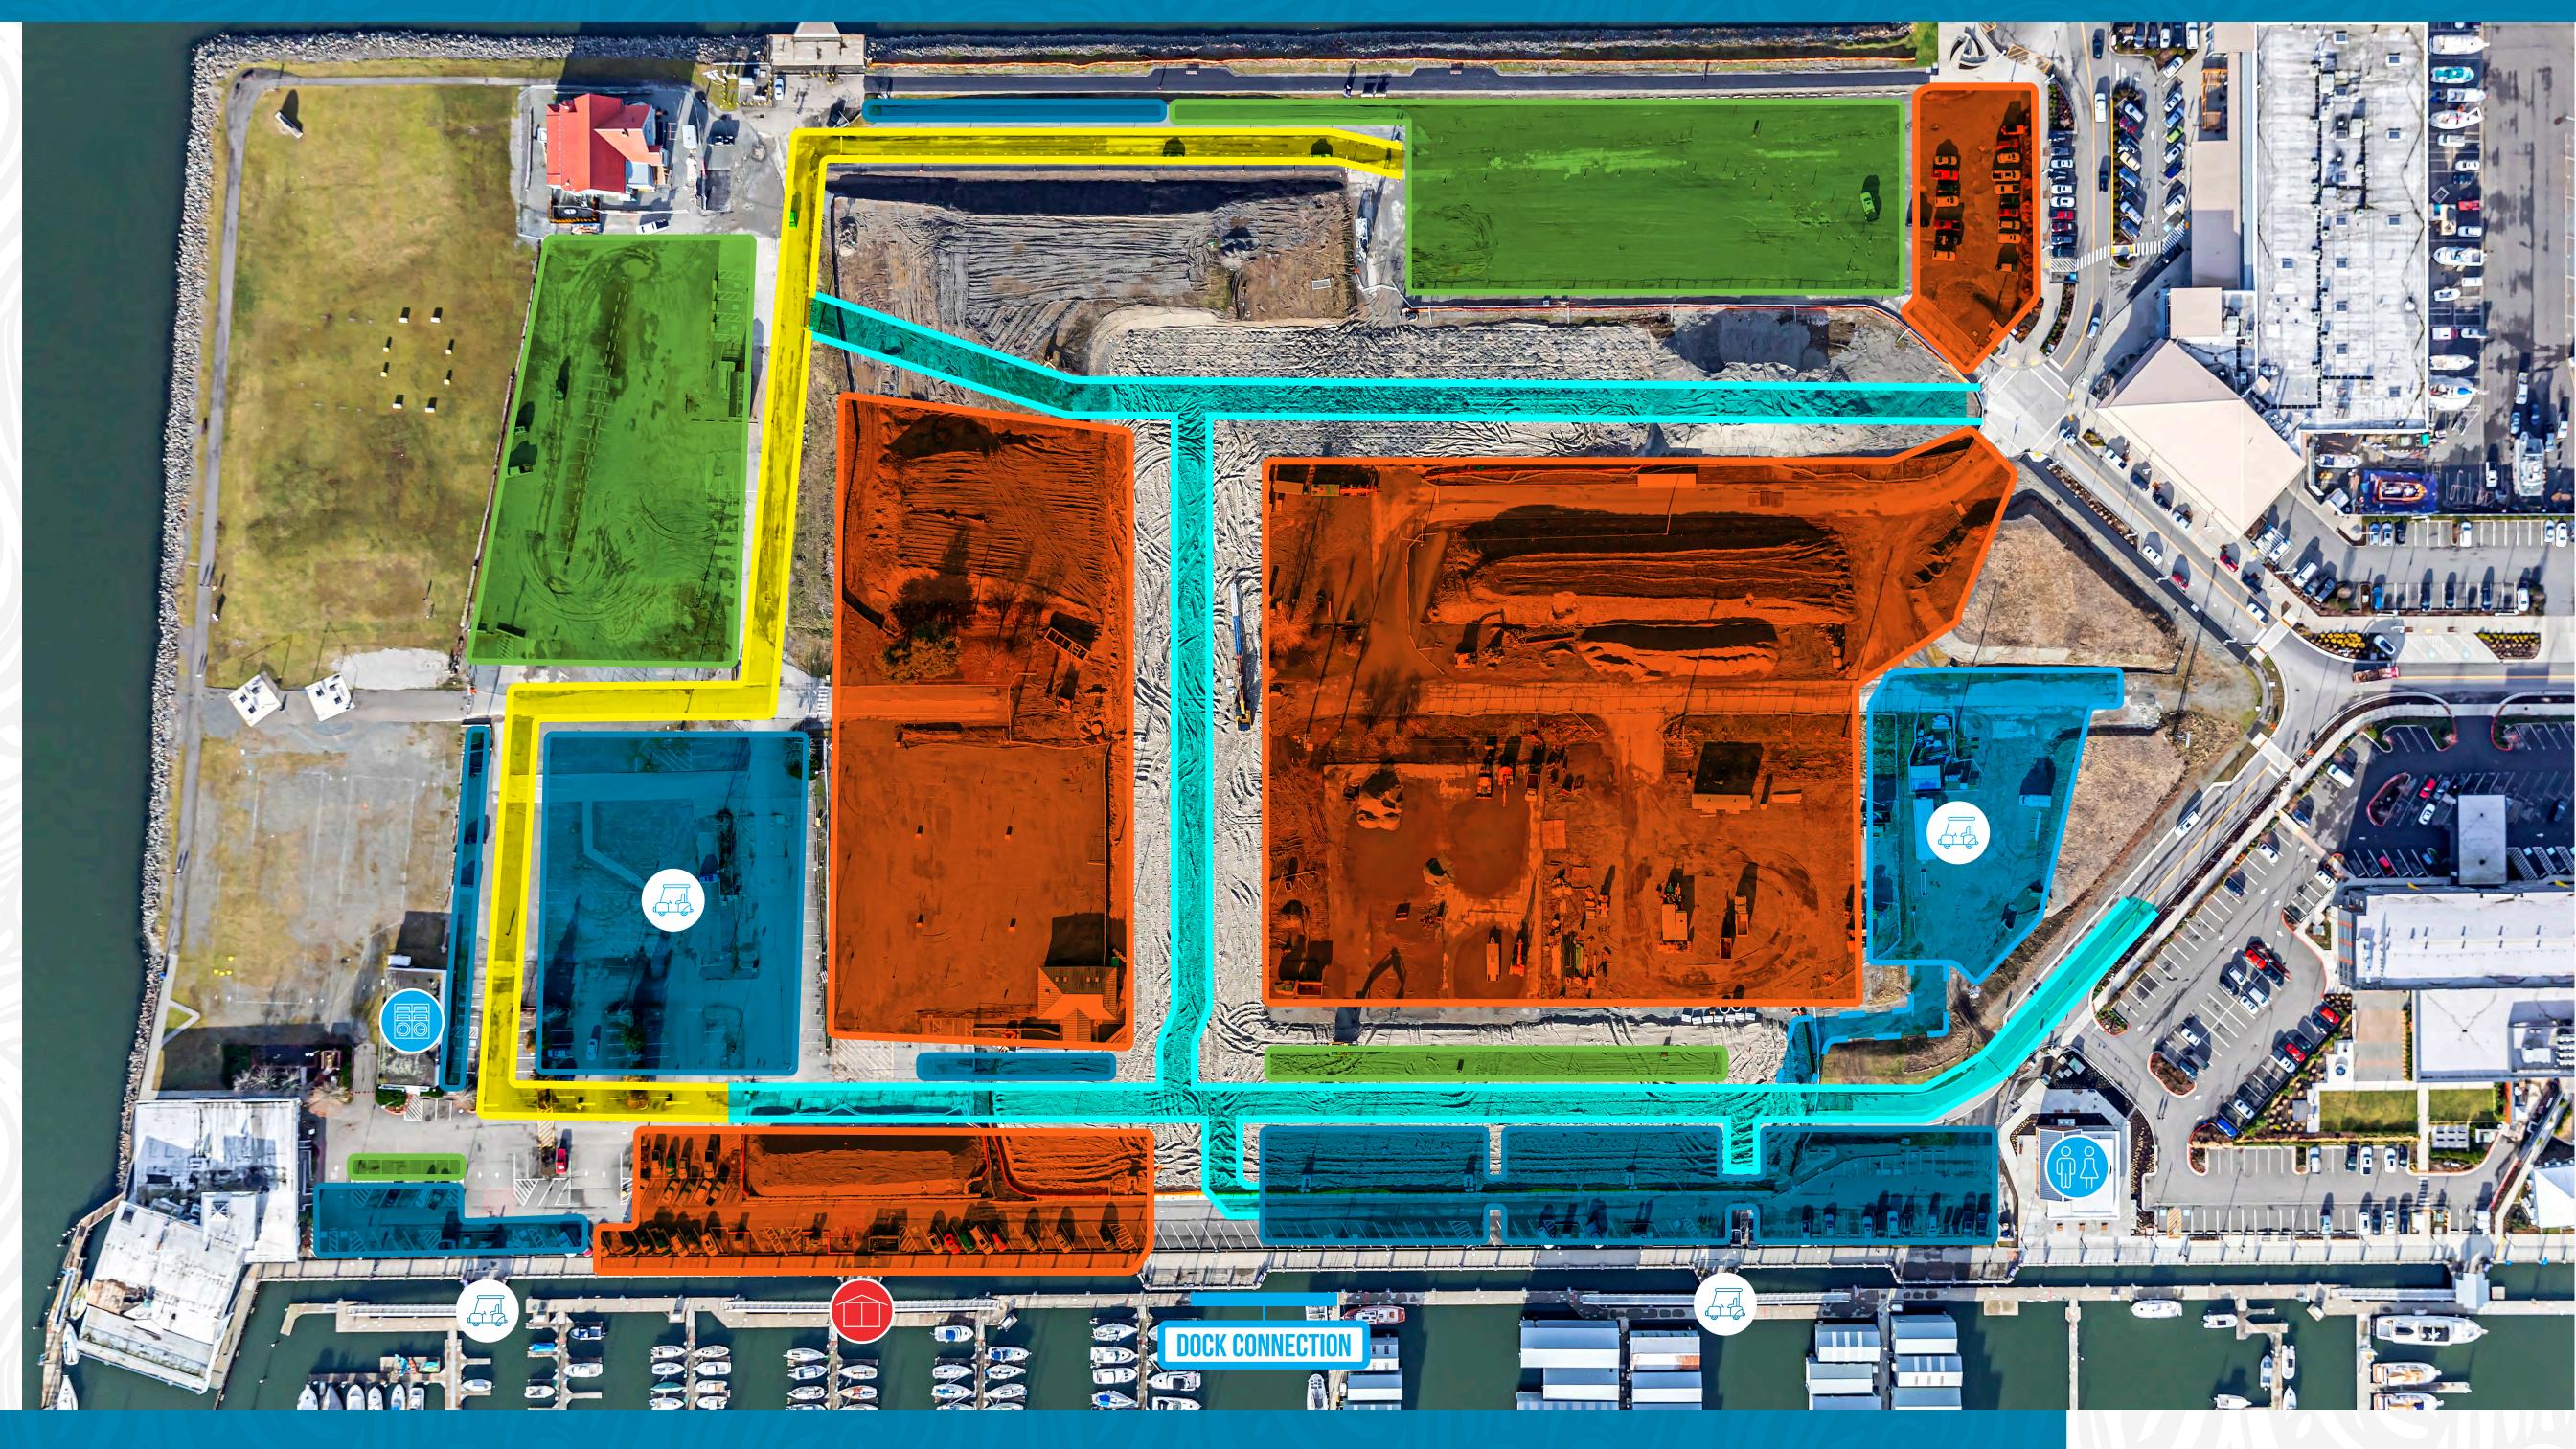



Port to continue shuttle service for boaters due to increased parking impacts. Service will continue until it is no longer in demand; more information to follow



New eastern Marina Slipholder Parking Lot open



Anticipate temporary 10-day closure of Central B – F Docks Gatehouse; advanced notice and alternate access provided







Two-way travel restored

#### **QUESTIONS?**

# MILLWRIGHT LOOP CONSTRUCTION SEQUENCING FINAL SITE | TIMELINE: END OF 2024

### FINAL PROJECT OUTCOME

- Two brand new gated marina tenant parking lots
- Complete roadway system and necessary utility connections for Millwright District private development
- Completed Esplanade expansion and two new vistas down to B/C Docks
- Marina visitor parking restored
- New garbage enclosures

### **PROJECT KEY**


MILLWRIGHT LOOP ROAD

COMPLETED ROAD

SLIPHOLDER PARKING

VISITOR PARKING

DEVELOPER LOT (POTENTIALLY UNDER CONSTRUCTION)

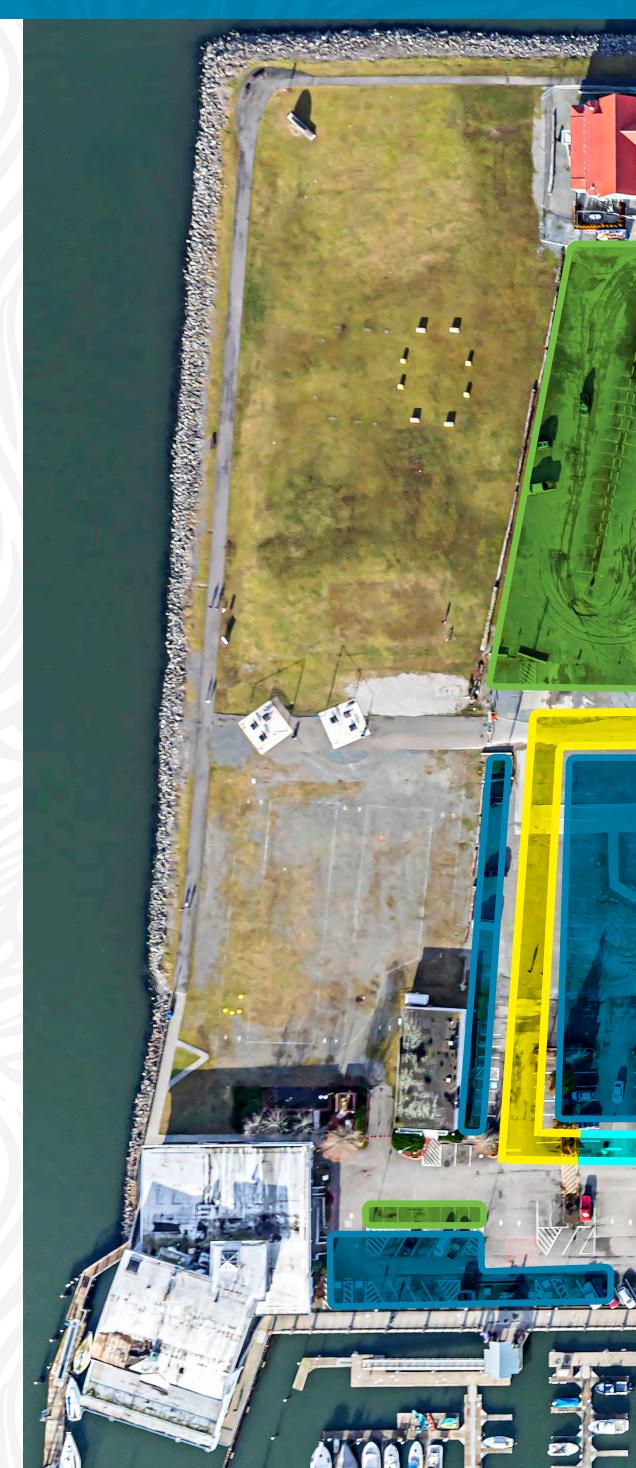



Central Marina laundry reopens



Central Marina restrooms and showers reopen



HILE





P

Two brand new gated marina tenant parking lots





#### **QUESTIONS?**
