




STATE ROUTE 99 SELMA TO FOWLER REHABILITATION PROJECT

McCall Avenue Undercrossing,
Selma to Merced Street
Undercrossing, Fowler



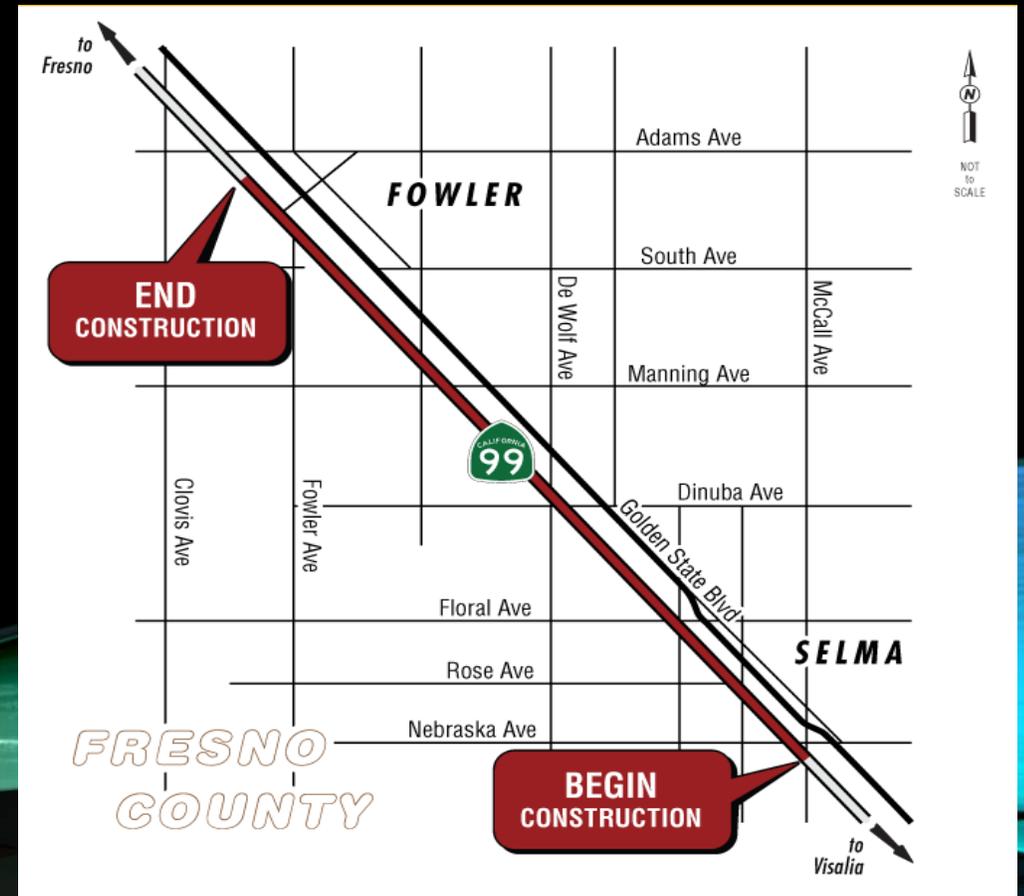

SCOPE OF WORK & SCHEDULE

- Limits of Work from McCall Avenue Undercrossing, Selma to Merced Street Undercrossing, Fowler
- Start of Construction July 2021
- Estimated Completion January 2024
- North Half of Project in the City of Fowler is Constructed
- Stage 5 (Phases 1-3) and Stage 6 (Phase 1-2)



STAGE 5

PHASE 1 (2 to 3 Week Duration)

Place K-Rail and Restripe NB and SB Lanes

Remove Sections of Concrete Barrier, Sign Structure and Footing Near Second Street

Replace Pavement and Concrete Barrier

No Ramps Closed in this Phase of Construction

PHASE 2 (2 to 3 Month Duration)

Place K-Rail and Restripe NB and SB Lanes

NB Lanes #1 and #2 Crossover Median into SB Inside Shoulder

SB Lanes Merge from 3 Lanes to 2 Lanes

NB Off-Ramp to Rte 43/Floral Ave. Closed this Phase of Construction

NB On-Ramp from Floral Ave. Closed this Phase of Construction

Message Board NB99 Directing Trucks to Exit at Mountain View Ave Exit

Remove and Replace Existing Pavement

Open Ramps Prior to Moving into the Next Phase of Construction

PHASE 3 (2 Month Duration)

Place K-Rail and Restripe NB Ramps

NB On-Ramp from NB Rte 43 Closed this Phase of Construction

NB On-Ramp from Second Street Closed this Phase of Construction

Remove and Replace Existing Pavement

Open Ramps Prior to Moving into Stage 6



STAGE 5 DETOUR MAP



DIST	COUNTY	ROUTE	POST MILES TOTAL PROJECT	SHEET NO.	TOTAL SHEETS
06	Fre	99	R4.9/11.6	135	657

REGISTERED CIVIL ENGINEER: **KAMRUL KHAN**
 DATE: 3-24-20
 PLANS APPROVAL DATE: 8-31-20
 THE STATE OF CALIFORNIA BY ITS OFFICERS OR AGENTS SHALL NOT BE RESPONSIBLE FOR THE ACCURACY OR COMPLETENESS OF SCANNED COPIES OF THIS PLAN SHEET.

PORTABLE CHANGEABLE MESSAGE SIGN
 NB 99 TO FLORAL CLOSED (P6)
 ONRAMP TO NB 99 (P7)
 USE DETOUR (P6)
 USE DETOUR (P7)

MOTORIST INFORMATION PLAN (NB ROUTE 99 OFF-RAMP TO FLORAL AVE CLOSED) (FLORAL AVE ON-RAMP TO NB ROUTE 99 CLOSED)
 NO SCALE
MI-5

UNIT 1512 PROJECT NUMBER & PHASE 0616000041

DATE PLOTTED: 05-27-20
 PLOTTED BY: 1512



STAGE 6

PHASE 1 (2 to 3 Month Duration)

Place K-Rail and Restripe NB and SB Lanes

SB On-Ramp from Rte 43/Floral Ave. Closed this Phase of Construction

SB Off-Ramp to Second Street Closed this Phase of Construction

SB Lanes #1 and #2 Crossover Median into NB Inside Shoulder

NB Lanes Merge from 3 lanes to 2 lanes

Remove and Replace Existing Pavement

Open Ramps Prior to Moving into the next Phase of Construction

PHASE 2 (2 Month Duration)

Place K-Rail and Restripe SB Ramps

SB Off-Ramp to SB Rte 43 Closed this Phase of Construction


SB Off-Ramp to Floral Ave. Closed this Phase of Construction

Remove and Replace Existing Pavement

Restripe at NB and SB Lanes and Open Ramps



STAGE 6 DETOUR MAP

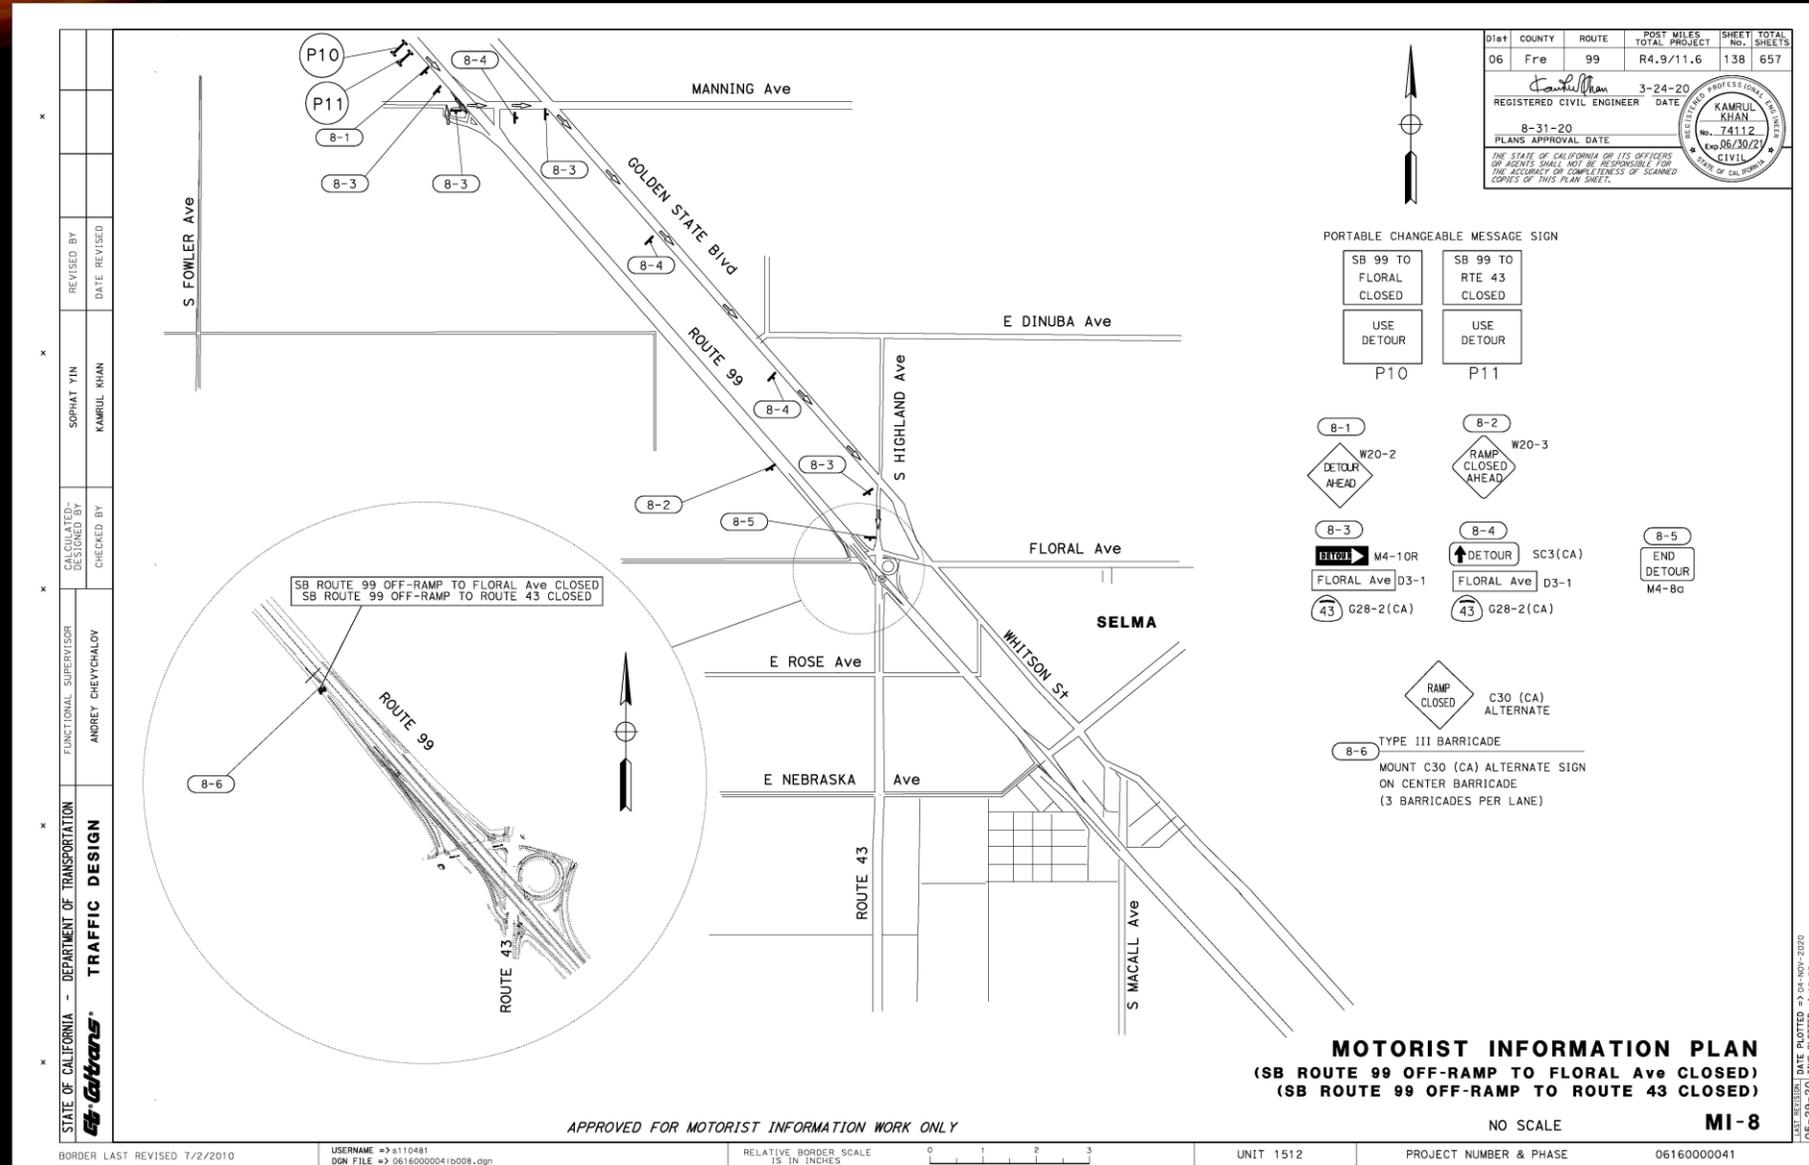



PROJECT SCHEDULE

BEGIN STAGE 5 CONSTRUCTION

Scheduled to Start on 04/02/2023 (Weather Permitting)

END STAGE 5 CONSTRUCTION

End Tentatively in August 2023



TRAFFIC MANAGEMENT

- 1. Truck Mounted Portable Changeable Message Signs.**
- 2. Automated End of Que System. Sensors at 4 set distance apart. Detects traffic speed and automatically provides warning messages. "Work Ahead", "Slow Down", "Traffic Stopped"**
- 3. Towing Service**
- 4. Temporary Lighting at ramps.**
- 5. Partnering with CHP through COZEEP**



PROJECT OUTREACH CAMPAIGN

- Project progress will be shared via project website
- Public Affairs will continue to communicate with city staff in Selma.
- Commuter Alerts for major ramp closures

State of California • Department of Transportation



COMMUTER ALERT

Date: Tuesday, March 7, 2023
District: 6 – Fresno, Kings, Tulare, Madera, Kern
Contact: Elizabeth Yelton | Office: 559-488-4067
Email: elizabeth.yelton@dot.ca.gov
Facebook: www.facebook.com/caltrans.centralvalleydistrict6
Twitter: www.twitter.com/caltransdist6

UPDATED: Tuesday, March 7, 2023

STATE ROUTE 99 SELMA TO FOWLER PROJECT SCHEDULED TO ENTER NEXT STAGE OF CONSTRUCTION

The California Department of Transportation (Caltrans) in cooperation with Security Paving Company, announces the next stage of the Selma to Fowler Rehabilitation Project.

During the next stage of the Selma to Fowler Project, work will take place between Second Street in the City of Selma and Manning Avenue in the City of Fowler. The following changes are expected to begin the week of **March 23, 2023**. This next stage of work is scheduled to be complete mid-May 2023. Please see the attached map of the detours that will be made available.

The following ramp and lane closures will be in place:

- **Northbound State Route 99:**
 - The northbound State Route 99 off-ramp to State Route 43/Floral Avenue will be closed. Commercial traffic is encouraged to utilize the Mountain View Avenue exit.
 - The Floral Avenue on-onramp to northbound State Route 99 will be closed.
- **Southbound State Route 99:**
 - The southbound lanes of State Route 99 between Manning Avenue and Second Street will be reduced from three lanes to two lanes.

Note: After completion of work on the above listed on and off-ramps, the ramps will be re-opened, and the following ramps will be closed:

- Northbound State Route 99 to Second Street off-ramp
- Northbound State Route 43 on-ramp to northbound State Route 99

Additional timeframes will be available as project completion advances.

Follow us on





THANK YOU
THIS CONCLUDES OUR
PRESENTATION

Contact:

Elizabeth Yelton (559) 916-8183

SR 99 Selma to Fowler Rehab

Project website:

<https://dot.ca.gov/caltrans-near-me/district-6/district-6-projects/06-0u420>

