

Permanent Patch Agreement

On the excavation permit application contractors are given the option to install a permanent patch instead of a temporary road patch. In addition to the road patch all other restorative work shall be completed at the time the permanent patch is installed – curbing, driveway repairs, sidewalk replacement, and turf establishment. If the permanent patch option is selected the patch and all associated restorative work will be inspected by the Engineering Department in the following spring. If all work is found to be acceptable, the restoration fee will be refunded to the contractor. The patch shall be free of defects including but not limited to settling, heaving, cracks, spalling, or raveling.

The joints must be sealed for the patch to be considered complete.

Initial

If the patch is unacceptable the contractor shall be notified and given ONE opportunity to repair the patch by May 15th of the current year.

Initial

If the Contractor fails to repair the patch as directed or if the repaired patch is still unacceptable the Town will repair the patch using the restoration fee deposit to pay for the work. The contractor shall be charged/refunded the difference between the restoration fee deposited and the actual cost of the repair.

Permanent Patch Specification: (refer to the attached drawing)


Permanent patch shall consist of 4-1/2" bituminous concrete class 2 (2" top course on 2-1/2" binder) on 12" of 3/4" processed aggregate. The joint shall be saw cut to a depth of 1/2" and sealed with liquid asphalt sealer (M 173).

By signing below you are agreeing to install a permanent patch in accordance with the Town of Southington's Permanent Pavement Detail (on reverse side).

Signature

Date

PERMANENT PAVEMENT DETAIL SEC. 4.06

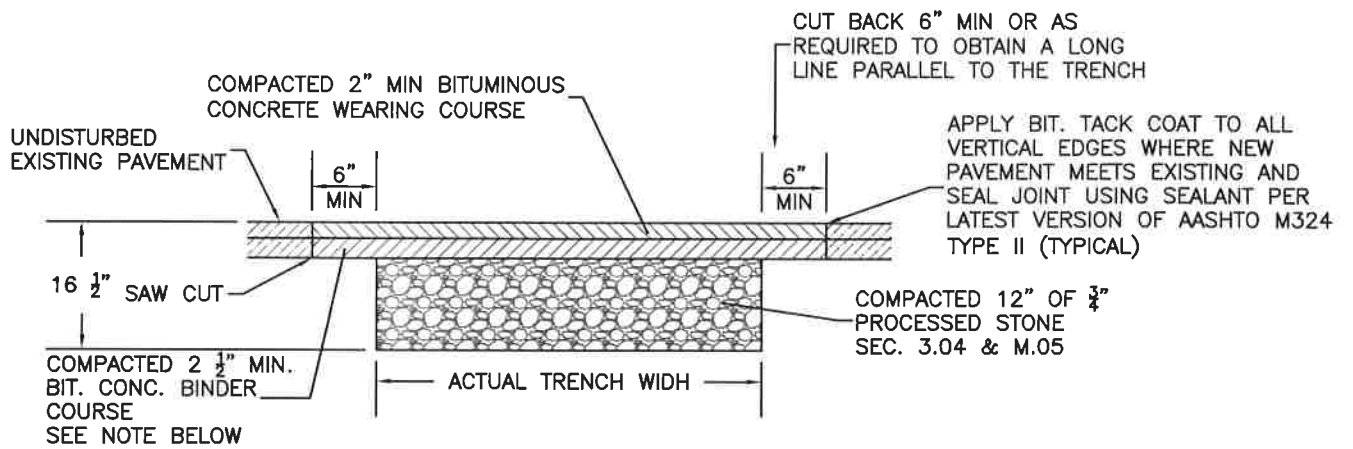

NOTE: WEARING COURSE SHALL BE CLASS II
BINDER COURSE SHALL BE CLASS II
SEC. 4.06 & M.04
PERMANENT PAVEMENT THICKNESS TO MATCH
EXISTING, IF GREATER THAN 4 $\frac{1}{2}$ "

ALL SPECS FROM DOT FORM 817
LATEST VERSION

TOWN OF SOUTHWINGTON			
PERMANENT PAVEMENT DETAIL			
MO. AUGUST	YR. 2019	SCALE HORIZ. N.T.S.	VERT. N/A
TOWN ENGINEER	S.E. HAYDEN	DATE	08/20/19
DRAWN BY	DPN	CHECKED BY	JAG
APPROVED BY	ERH	DATE	08/20/19
